

Baton Rouge SSO Program

Progress Report



April 2011




Prepared for
City of Baton Rouge/
East Baton Rouge Parish
Department of Public Works

Prepared by
CH2MHILL

In association with
SIGMA Consulting Group, Inc.
ILSI Engineering

BATON ROUGE 
Program

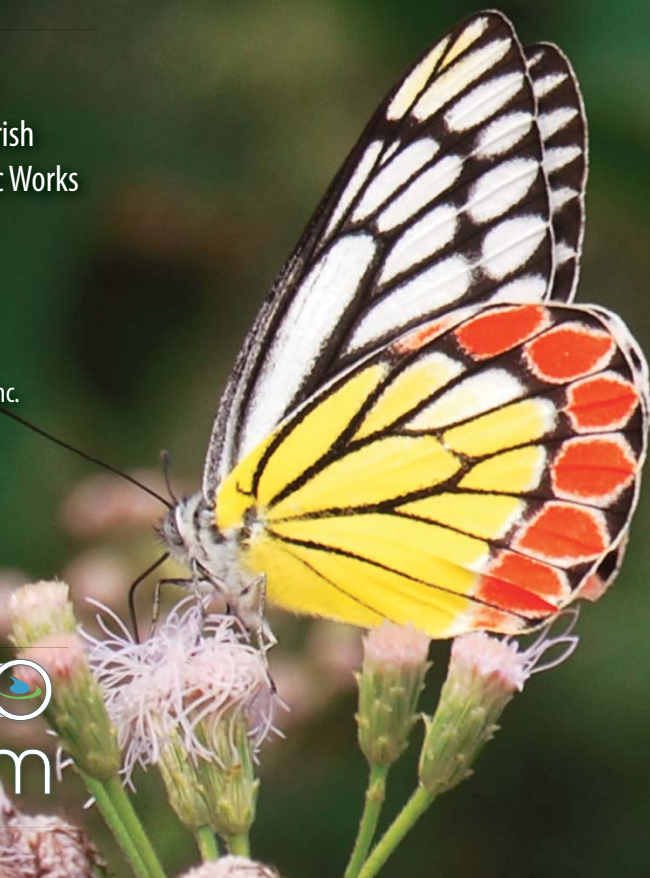



Program Management



The Baton Rouge Sanitary Sewer Overflow (SSO) Program is a comprehensive sewer infrastructure improvement project. The program involves implementing the design and construction of projects to rehabilitate sewer pipelines, improve or install new pump stations, increase storage capacity, and upgrade facilities at the North and South Wastewater Treatment Plants (WWTPs).

Program Highlights

- 80 Active Projects
 - » 15 Projects Completed
 - » 30 Projects Under Construction
 - » 35 Projects in Design



Keeping You Informed
During Construction is
Important to Us

Call **225.588.5678**
with any
construction-related
questions

Parishwide SSO Program Projects Improve Quality of Life for Residents


Rehabilitation projects will improve more than 5,500,000 linear feet (lf) of gravity sewer pipe (1,042 miles) and 20,000 manholes.

Three treatment plant projects at the South WWTP will increase capacity to handle increased flows during and after storm events.

Capacity projects include upgrades or installation of 152 pump stations and improvements to 350,000 lf of gravity sewer (66 miles) and 670,000 lf forcemain (127 miles).

Three collection system wet weather storage projects involve adding 20 million gallons (MGs) of storage in the Zachary Area Transmission Network; 26 MG of storage, 25,000 lf of forcemain and three pump stations at the Choctaw Storage and Pump Station Facility; 56 MG of storage in the North WWTP basin; and 10 MG of storage at Hooper Road.





In the Spotlight...

Promoting Local, Small, and Disadvantaged Businesses

The Office of the Mayor-President, the Department of Public Works (DPW), and the SSO Program Management Team are working in partnership to strengthen local business capacity and encourage participation on Program projects. SSO Program staff routinely meets with small and disadvantaged businesses in Baton Rouge who are interested in providing services and participating on the Program. Business owners are provided information on Program contractors, upcoming projects, registering with the City-Parish's database, and available support and resources. Program staff also assists business owners in developing capabilities statements and provide instructions on how to access solicitations for services through RFQ Manager (for Design Consultants) and BIDX (for Contractors).

Registering to Receive RFQs

As new Request for Qualifications (RFQs) are advertised through the Advocate newspaper, Design Consultants can subscribe to the RFQ Manager and receive notices when new DPW projects are available to receive RFQs.

1. Access <http://www.brprojects.com/rfqmanager/>
2. Register as a new user
3. Select the categories for which you would like to receive RFQ notices
4. Review RFQs that are automatically sent to your e-mail and determine whether you want to submit an RFQ for it.

To submit the RFQ, follow the directions in the Public Notice, using the allotted forms for the Statement of Qualification, before or by the specified deadline.

Registering to Receive Construction Advertisements

Construction Contractors registering through BIDX should log-on to the online bidding exchange web site at www.bidx.com.

1. Establish your account with a valid username and password (note there is a monthly fee involved). Alternately, paper copies of the SSO project plans, specifications, and contract documents are on file at DPW and may be obtained upon payment of the designated fee.
2. Understand the construction project being advertised, including pre-bid meeting date and bid due date.
3. Attend a mandatory pre-bid conference held at the date and time described in the Notice to Contractors.
4. Submit electronic bids and electronic bonds through www.bidx.com or in person at DPW Purchasing Department prior to the bidding deadline.

SSO Projects are advertised in the Advocate newspaper under public notices/bids/proposals and also posted on the SSO web-site at http://www.brprojects.com/sewer/pages/contractor_calendar.htm to view a copy of all SSO projects advertised for design and/or construction.

When projects are advertised for construction, they are also included in DPW's purchasing web site at: <http://www.brgov.com/dept/purchase/bids.asp>.

Project Information

Project Components

Consultant/Contractor Information Cost

Schedule

	#	Project Name	Project Type		DPW Project #	Number of Upgraded Pump Stations	Number of Replaced/Rehabilitated Manholes*	Linear Feet of Force Main Improvements	Linear Feet of Gravity Main Improvements	Design Consultant	Construction Contractor	Construction Contract Amount	Project Start	Advertise for Construction Bid	Project End	
COMPLETED PROJECTS	1	Jefferson Highway - Hoo Shoo Too Road	PDP	Rehab	07-AR-US-0049	-	553	-	-	DPW	Allen & LeBlanc	\$1,769,438	5/16/2007	6/27/2008	9/22/2009	
	2	Staring Lane - Boone Drive	PDP	Rehab	08-AR-UF-0004	-	665	-	139,050	CSRS, Inc.	Grady Crawford	\$5,416,540	11/27/2007	1/23/2009	5/3/2010	
	3	Staring Lane FM (PH1 - Burbank to Highland)	PDP	Capacity	06-WC-CP-0036	-	-	2,260	-	Monroe & Corie	James Construction	\$4,615,500	1/11/2008	9/19/2008	7/2/2010	
	4	Gurney Road - Joor Road	PDP	Capacity	07-PS-BD-0017	1	-	14,475	-	Neel-Schaffer	Grady Crawford	\$1,543,734	1/18/2008	8/29/2008	10/15/2009	
	5	RMAP1 - Kleinpeter Area Upgrades	***	RMAP1	03-RMP-S14	1	-	2,000	-	Monroe & Corie	Allen & LeBlanc	\$324,024	2/1/2008	7/14/2008	5/8/2009	
	6	RMAP1 - PS136 Area Upgrades	***	RMAP1	99-RMP-S16	9	-	27,700	20,700	Sigma Consulting	Nottingham Construction	\$8,994,709	2/1/2008	10/26/2008	9/15/2010	
	7	Comite Drive - Foster Road - Phase 1	PDP	Capacity	07-PS-BD-0019	3	-	12,080	-	Monroe & Corie	Hemphill Construction	\$1,923,521	3/3/2008	1/16/2009	6/30/2010	
	8	25 th Street - North Acadian Thruway	PDP	Capacity	09-GS-UF-0008	-	-	-	-	Hartman Engineering	(design only)	(design only)		2/2/2009	-	3/4/2010
	9	NWWTP Odor Control	PDP	WWTP	07-WP-TP-0030	-	-	-	-	Environmental Eng Svcs	SEMS, Inc.	\$5,363,052	6/29/2007	10/30/2009	11/19/2010	
	10	Foster Road - Hooper Road	PDP	Capacity	07-FM-BD-0046	-	-	26,200	-	PEC	Hemphill Construction	\$8,761,675	2/14/2008	1/9/2009	11/30/2010	
	11	Burbank Road - Gardere Lane	PDP	Rehab	08-AR-UF-0003	-	787	-	168,300	CSRS, Inc.	Allen & LeBlanc	\$6,126,533	5/16/2007	11/14/2008	1/3/2011	
	12	RMAP1 - Industriplex Area Upgrades	***	RMAP1	99-RMP-S08	6	-	4,000	-	Forte & Tablada	BRH Garver	\$10,018,093	3/10/2008	10/31/2008	1/31/2011	
	13	Comite Drive - Foster Road - Phase 2	**	Capacity	02-CS-HC-0001	-	-	-	1,361	Monroe & Corie	JB James Construction	\$895,957	6/23/2008	6/27/2009	3/17/2011	
	14	Sullivan Rd/Lovett Rd/Wax Rd	PDP	Capacity	07-PS-BD-0018	3	-	4,200	2,100	Hartman Engineering	Don M. Barron Contractor	\$2,158,346	1/17/2008	1/16/2009	3/17/2011	
	15	SWWTP IAPs Combined	PDP	WWTP	08-TP-BD-0031	-	-	-	-	CDM, MWH, URS Corp.	Brasfield & Gorrie	\$27,363,571	11/6/2006	12/12/2008	4/8/2011	
					23	2,005	92,915	331,511				\$85,274,694				
UNDER CONSTRUCTION	1	Elm Grove Garden Road - Harding Blvd	PDP	Rehab	09-AR-BD-0012	-	839	-	199,500	CSRS, Inc.	Allen & LeBlanc	\$12,989,271	10/1/2008	9/25/2009	6/13/2011	
	2	Scotland Avenue - Progress Road	PDP	Rehab	09-AR-BD-0011	-	300	-	208,000	CSRS, Inc.	Magnolia Construction	\$9,207,594	9/9/2008	9/25/2009	6/14/2011	
	3	Group Project 2 - Small Pump Stations	PDP	Capacity	08-PS-IF-0046	7	-	-	-	ABMB Eng.	Grady Crawford	\$3,475,914	3/10/2008	3/26/2010	8/16/2011	
	4	Nicholson Dr - Highland Rd - Perkins Rd - Phase A	PDP	Capacity	09-FM-MS-0047A	-	20	8,400	3,400	Buchart - Horn	Grady Crawford	\$2,591,613	6/29/2009	10/29/2010	9/28/2011	
	5	Oak Villa Blvd - Choctaw Street	PDP	Rehab	08-AR-UF-0005	-	990	245,000	-	CSRS, Inc.	Grady Crawford	\$8,997,369	4/14/2008	5/15/2009	10/5/2011	
	6	Highland Road - Buchanan Street	PDP	Capacity	08-GS-ST-0021	-	-	4,465	8,390	Burk-Kleinpeter/Justice & Huang (JV)	Gilmore & Sons Construction	\$4,325,851	3/14/2008	4/23/2010	10/5/2011	
	7	Foster Drive - Government Street - Phase A	PDP	Rehab	09-AR-BD-0015A	-	629	-	80,600	CSRS, Inc.	Grady Crawford	\$4,819,752	5/25/2009	6/25/2010	10/20/2011	
	8	Citilace/Essex Area - PS119 and FM Improvements	PDP	Capacity	08-FM-UF-0024	1	-	8,100	-	GSA Consulting Engineers, Inc.	BRH Garver	\$2,801,502	2/25/2008	8/20/2010	1/3/2012	
	9	South Blvd-St. Joseph St / 25th St - N. Acadian Thruway	PDP	Capacity	08-GS-ST-0018	-	-	18,360	3,000	Evans-Graves	Reynolds, Inc.	\$17,965,049	3/27/2008	4/16/2010	1/12/2012	
	10	Downtown Area - PS15, PS19, PS59, PS60	PDP	Capacity	08-PS-ST-0056/57	3	-	-	-	Shaw Environmental & Infrastructure, Inc.	Guy Hopkins Construction Co.	\$4,841,000	3/24/2008	9/3/2010	2/2/2012	
	11	Foster Drive - Government Street - Phase B	**	Rehab	09-AR-BD-0015B	-	-	-	78,700	CSRS, Inc.	Insituform Technologies	\$2,863,100	5/25/2009	9/17/2010	2/17/2012	
	12	Capitol Lake Dr - Gayosa St / 25 th St - N. Acadian Thruway	PDP	Capacity	07-PS-BD-0048	-	-	19,320	19,150	Shread-Kuykendall & Associates, Inc.	Morgan Contracting, Inc. of FL	\$10,497,568	1/14/2008	6/18/2010	2/17/2012	
	13	Kenilworth Blvd - Boone Drive	PDP	Rehab	09-AR-BD-0014	-	1,159	-	72,000	CSRS, Inc.	Allen & LeBlanc	\$5,168,129	3/26/2009	10/8/2010	4/4/2012	
	14	Silverleaf Road - Ford Street	PDP	Rehab	10-AR-BD-0041	-	-	-	115,200	CSRS, Inc.	John Plott Company	\$8,024,945	10/26/2009	1/28/2011	4/12/2012	
	15	Sharp Road - Florida Blvd	PDP	Rehab	09-AR-BD-0013	-	1,154	-	274,475	CSRS, Inc.	Reynolds, Inc.	\$17,492,855	1/15/2009	4/16/2010	7/6/2012	
	16	Bluebonnet Blvd - Jefferson Hwy - Phase 1	PDP	Rehab	10-AR-UF-0042	-	-	-	54,200	CSRS, Inc.	Allen & LeBlanc	\$3,848,872	2/8/2010	3/18/2011	7/19/2012	
	17	Brookstown Road - Evangeline Street - Phase 2	PDP	Rehab	10-AR-BD-0040	-	1,075	-	84,000	CSRS, Inc.	John Plott Company	\$5,467,640	10/8/2009	11/12/2010	10/4/2012	
	18	Highland Road - Burbank Drive	PDP	Capacity	08-FM-ST-0023	-	-	39,400	-	GOTECH, Inc.	RACON, Inc.	\$20,591,067	3/31/2008	10/29/2010	12/12/2012	
	19	Multiple PS - Jefferson Highway - Park Forest Drive	PDP	Capacity	09-PS-MS-0046	6	-	-	-	CSRS, Inc.	Grady Crawford	\$2,922,472	6/8/2009	3/25/2011	12/12/2012	
	20	Brookstown Road - Evangeline Street - Phase 1	PDP	Rehab	10-AR-BD-0039	-	1,150	-	161,000	CSRS, Inc.	Grady Crawford	\$10,309,180	7/10/2009	10/15/2010	12/14/2012	
	21	Group Project 1A (Veterans Parkway - Gravity Mains)	PDP	Capacity	08-GS-UF-0053	-	-	-	46,000	URS Corp.	Texas Sterling Const. Co.	\$19,581,108	3/10/2008	10/29/2010	1/4/2013	
	22	Choctaw Storage and PS Facility	PDP	WWTP	09-PS-UF-0009	3	-	25,000	-	CDM	Brasfield & Gorrie	\$43,237,000	4/14/2008	10/22/2010	2/7/2013	
	23	Zachary Area Transmission Network - Phase 4	PDP	Capacity	10-FM-IF-0005	-	-	42,500	-	SJB/Owen & White	Wicker Construction	\$7,091,115	3/24/2008	8/27/2010	2/11/2013	
	24	SWWTP Wet Weather Improvements - Phase 1	PDP	WWTP	08-TP-BD-0033	-	-	-	-	CDM	Brasfield & Gorrie	\$108,443,892	6/23/2008	3/26/2010	4/18/2013	
	25	Perkins/Old Perkins Area - Booster PS S14 Improvements	PDP	Capacity	09-PS-MS-0034	1	-	-	-	GEC	(bid opening on 5/10/11)	TBA	4/24/2009	4/8/2011	5/22/2013	
	26	Zachary Area Transmission Network - Phase 3	PDP	Capacity	10-FM-IF-0004	-	-	27,000	-	SJB/Owen & White	Hemphill Construction	\$8,947,920	3/24/2008	10/15/2010	6/17/2013	
	27	Zachary Area Transmission Network - Phase 1	PDP	Capacity	10-FM-IF-0002	3	-	-	-	SJB/Owen & White	Max Foote Construction	\$18,486,500	3/24/2008	8/20/2010	7/17/2013	
	28	Staring Lane FM (Phase 2 - Highland to Perkins)	PDP	Capacity	06-WC-CP-0036	-	-	12,363	-	Monroe & Corie	JB James Construction	\$9,892,090	4/4/2008	8/6/2010	7/30/2013	
	29	Emergency Generators Purchasing	***	Other	09-PS-BD-0037	-	-	-	-	N/A	ARCCO	\$19,100,000	2009	6/18/2010	10/17/2013	
	30	Emergency Generators Installation	***	Other	09-PS-BD-0037	-	-	-	-	N/A (installation only)	Grady Crawford	\$7,113,634	2010	-	2013	
					24	7,316	449,908	1,407,615				\$401,094,004				

* All manholes are inspected in the project area. Only some are rehabilitated or replaced.

** These projects are included in the Program Delivery Plan (PDP), however are not shown as phases A/1 and B/2. During design, it was determined that these projects should be split into phases for better constructability.

*** These projects are not included in the PDP, however are either Remedial Measures Action Plan 1 projects (RMAP1) or are projects identified in the Wastewater Master Plan (not part of the EPA Consent Decree)

Project Information				Design Consultant	Cost	Schedule			
#	Project Name	Project Type		DPW Project #	Company	Estimated Construction Value	Project Start	Advertise for Construction Bid	Project End
1	Zachary Area Transmission Network Imp - Gen. Design	PDP	WWTP	N/A	SJB/Owen & White	\$0 (design only)	3/24/2008	-	5/31/2011
2	Central Consolidation- PS42 FM - Phase A	PDP	Capacity	09-FM-MS-0036A	SJB/Owen & White	\$16,610,000	11/7/2008	4/29/2011	5/20/2013
3	Bluebonnet Blvd - Jefferson Hwy - Phase 2	PDP	Rehab	10-AR-MS-0043	CSRS, Inc.	\$6,685,000	3/23/2010	4/29/2011	7/31/2012
4	Staring Lane FM (PhIII - Perkins to PS58)	PDP	Capacity	06-WC-CP-0036	Monroe & Corie	\$9,550,000	4/30/2009	5/20/2011	2/10/2014
5	Nicholson Dr - Highland Rd - Perkins Rd - Phase B	**	Capacity	09-FM-MS-0047	Buchart - Horn	\$7,965,000	6/29/2009	5/20/2011	5/7/2012
6	Government St - S. Acadian Thruway	PDP	Capacity	09-GS-MS-0043	GSA Consulting Engineers, Inc.	\$4,680,000	8/28/2009	5/27/2011	2/7/2013
7	Acadian Thruway - Perkins Road	PDP	Rehab	10-AR-BD-0044	CSRS, Inc.	\$3,915,500	5/31/2010	5/27/2011	9/24/2012
8	Zachary Area Transmission Network Improvements - Phase 2	PDP	Capacity	10-FM-IF-0003	SJB/Owen & White	\$14,583,700	3/24/2008	6/24/2011	6/7/2013
9	Stanford Avenue - Morning Glory Road	PDP	Rehab	10-AR-BD-0045	CSRS, Inc.	\$6,876,000	6/25/2010	6/24/2011	11/2/2012
10	Central Consolidation FM (2,3,5,7,10)	PDP	Capacity	09-FM-MS-0033	Shread-Kuykendall & Associates, Inc.	\$10,601,000	11/7/2008	7/15/2011	8/20/2013
11	Bayou Duplantier Area Sewer Upgrades	PDP	Capacity	09-GS-MS-0042	Neel-Schaffer	\$4,374,000	8/31/2009	7/15/2011	8/28/2013
12	Central Consolidated Pump Stations (2,3,4,5,6,7,10 and 91)	PDP	Capacity	09-PS-MS-0035	Burk Kleinpeter / JIG	\$16,592,000	11/7/2008	7/29/2011	3/31/2014
13	Group Project 1B (Veterans Parkway - PS and FM)	PDP	Capacity	08-PS-UF-0054	Evans-Graves / Burk Kleinpeter	\$19,309,000	3/10/2008	8/12/2011	1/24/2014
14	SWWTP Wet Weather Improvements - Phase 2	PDP	WWTP	08-TP-BD-0055	MWH	\$107,219,000	10/1/2008	8/19/2011	12/31/2014
15	Acadian Thruway - Claycut Road	PDP	Rehab	10-AR-BD-0046	CSRS, Inc.	\$7,449,000	8/2/2010	8/19/2011	11/29/2012
16	Central Pump Station - PS 42	PDP	Capacity	09-PS-UF-0003	MWH	\$6,695,070	10/21/2008	8/26/2011	9/27/2013
17	Central Consolidation- PS42 FM - Phase B	**	Capacity	09-FM-MS-0036B	SJB/Owen & White	\$11,600,000	11/7/2008	9/9/2011	7/8/2013
18	PS 58 Overflow Pump Station	PDP	Capacity	09-PS-UF-0001	GEC	\$15,750,000	1/5/2009	9/9/2011	2/21/2014
19	Highland Road - Washington Street	PDP	Rehab	TBA	CSRS, Inc.	\$8,022,000	10/13/2010	9/9/2011	12/28/2012
20	O'Neal Lane Pipeline Projects - Phase A	PDP	Capacity	10-FM-MS-0008A	URS Corp.	\$12,157,000	9/29/2009	9/16/2011	2/28/2014
21	O'Neal Lane Pipeline Projects - Phase B	**	Capacity	10-FM-MS-0008B	URS Corp.	\$5,300,000	9/29/2009	9/16/2011	2/28/2014
22	Multiple PS - Nicholson Dr - Brightside Dr	PDP	Capacity	09-PS-MS-0048	Arcadis U.S., Inc.	\$6,113,000	9/14/2009	9/19/2011	2/28/2014
23	Plank Road - Kleinpeter Road	PDP	Capacity	09-GS-UF-0028	Forte & Tablada	\$7,583,000	3/23/2009	10/28/2011	1/10/2014
24	Hooper Storage	PDP	WWTP	09-PS-UF-0007	TRC Engineers	\$19,115,000	1/19/2009	11/11/2011	12/24/2013
25	Airline Highway Pipeline Projects	PDP	Capacity	10-GS-MS-0007	ABMB Eng.	\$35,200,000	1/30/2009	1/13/2012	12/31/2014
26	Lovett Road - Greenwell Springs - Phase A	PDP	Capacity	10-FM-MS-0049A	SJB/Owen & White	\$13,364,000	5/3/2010	6/15/2012	12/31/2014
27	Lovett Road - Greenwell Springs - Phase B	**	Capacity	10-FM-MS-0049B	SJB/Owen & White	\$8,780,000	5/3/2010	6/15/2012	12/31/2014
28	Hooper Road Pump Station	PDP	Capacity	10-PS-MS-0048	Stanley	\$11,935,000	5/3/2010	7/6/2012	12/31/2014
29	O'Neal Lane Pump Stations - Phase A	PDP	Capacity	10-PS-MS-0050	MWH	\$12,226,000	5/25/2010	7/13/2012	12/31/2014
30	O'Neal Lane Pump Stations - Phase B	PDP	Capacity	10-PS-MS-0051	URS Corp.	\$9,800,000	5/25/2010	7/13/2012	12/31/2014
31	Multiple PS - Highland Rd - Kenilworth Parkway	PDP	Capacity	10-PS-MS-0009	AECOM	\$8,926,760	2/8/2010	10/5/2012	12/31/2014
32	Florida Blvd Pump Station Improvements	PDP	Capacity	11-PS-MS-0003	Brown & Caldwell	\$15,000,000	1/28/2011	10/5/2012	12/9/2014
33	Highland Road Pipeline Improvements - Phase A	PDP	Capacity	11-ES-PW-0002A	Evans Graves	\$9,741,000	1/28/2011	10/26/2012	4/11/2014
34	Highland Road Pipeline Improvements - Phase B	**	Capacity	11-ES-PW-0002B	Evans Graves	\$8,118,000	1/28/2011	10/26/2012	4/11/2014
35	Sherwood Forest Blvd - Goodwood Blvd Pipeline Improvements	PDP	Capacity	11-FM-MS-0005	Forte & Tablada	\$10,200,000	3/28/2011	6/7/2013	12/31/2014

\$472,035,030

** These projects are included in the Program Delivery Plan (PDP), however are not shown as phases A and B. During design, it was determined that these projects should be split into phases for better constructability.

LOOKING AHEAD...

Projects Recently Advertised for Construction Bids

The following projects advertised for construction bids in April 2011:

Bluebonnet Blvd – Jefferson Highway Phase 2 Comprehensive Rehabilitation Project.

Estimated Construction Cost - \$6,685,000. Advertised April 29, 2011; Mandatory Pre-Bid Meeting May 16, 2011; Construction Bids Due May 24, 2011.

Central Consolidation Pump Station 42 Forcemain Capacity Improvement Project Phase A.

Estimated Construction Cost - \$16,610,000. Advertised April 29, 2011; Mandatory Pre-Bid Meeting May 18, 2011; Construction Bids Due June 2, 2011.

Perkins/Old Perkins Area – BPS 514 Improvements Capacity Improvement Project.

Estimated Construction Cost - \$10,397,000. Advertised April 8, 2011; Mandatory Pre-Bid Meeting April 26, 2011; Construction Bids Due May 10, 2011.

Projects to be Advertised for Construction Bids:

The following projects are expected to advertise for construction bids in May 2011:

- Staring Lane FM (Phase III – Perkins to PS58) Capacity Improvement project
- Government Street – South Acadian Thruway Capacity Improvement Project
- Acadian Thruway – Perkins Road Comprehensive Rehabilitation Project

Projects to be Advertised for Engineering Selection:

Plank Road Pump Station Capacity Improvement Project

Estimated Construction Cost - \$9,300,000. This project consists of replacing five and upgrading three pump stations. Expected to advertise for RFQ in May 2011.

Multiple PS – Burbank Drive – Siegen Lane Capacity Improvement Project

Estimated Construction Cost - \$4,100,000. The project includes replacement of six pump stations. The new pump stations will work in conjunction with the forcemain upgrades in other South Forced Lower Basin projects to alleviate chronic SSOs at and near these pump stations. Expected to advertise for RFQ in May 2011.

Oak Villa Blvd – Monterey Blvd Capacity Improvement Project

Estimated Construction Cost - \$9,000,000. This project includes the upsizing of the gravity sewer upstream of PS16, PS50, and PS51 and the forcemain from PS16, which is being upgraded as part of the Multiple PS – Florida Blvd – Sherwood Forest Blvd project. Expected to advertise for RFQ in May 2011.

Joor Road – Greenwell Springs Capacity Improvement Project

Estimated Construction Cost - \$6,900,000. This project involves the design and construction of forcemain upgrades in the North Forced West Basin. The upgrades are designed to alleviate chronic SSOs at the pump stations and increase the forcemain capacity. The upgrades range in size from 6 to 24 inches in diameter. Expected to advertise for RFQ in May 2011.

For more information, please visit the project website at www.brprojects.com



BATON ROUGE SSO PROGRAM PROGRESS REPORT

APRIL 2011

300 North Boulevard, Room 208

Baton Rouge, LA 70802

(225) 389-3158

DPW@brgov.com

BATON ROUGE SSO
Program

Printed on Recycled Paper

